


ACTIVE PROJECTS BY THE NUMBERS



ACTIVE PROJECT STATUSES

- **Planning** - Project plans are documented, the project deliverables and requirements are defined with stakeholders and reviewing agencies, and the project schedule is created.
- **Scope Development** - A comprehensive scope suitable for design or design-build procurement is being developed for the approved project.
- **Design Procurement** - Services are being solicited for architectural/engineering services to complete design documents.
- **Design** - Project is being designed by the Architect/Engineer and going through the necessary review & approval processes.
- **Contractor Procurement** - Construction services are being solicited.
- **In Construction** - The construction work is awarded to a Contractor and preconstruction (e.g., material ordering) and/or active construction is underway.
- **Substantial Completion** - Construction work is sufficiently completed with all requisite inspections & approvals obtained for use and/or occupancy.
- **Final Completion (Closeout Approval Requested)** - Project manager has fully accepted contract work AND punch list/corrective work is 100% complete; any required trade permits/inspections are 100% approved; applicable operating manuals, as-builts & warranty information are on hand; and, final payment is approved.

Active Projects By Status	#
Planning	29
Scope Development	10
Design Procurement	4
Design	23
Contractor Procurement	51
In Construction	48
Substantially Complete	73
Final Completion (Closeout Approval Requested)	157
TOTAL ACTIVE PROJECTS	395

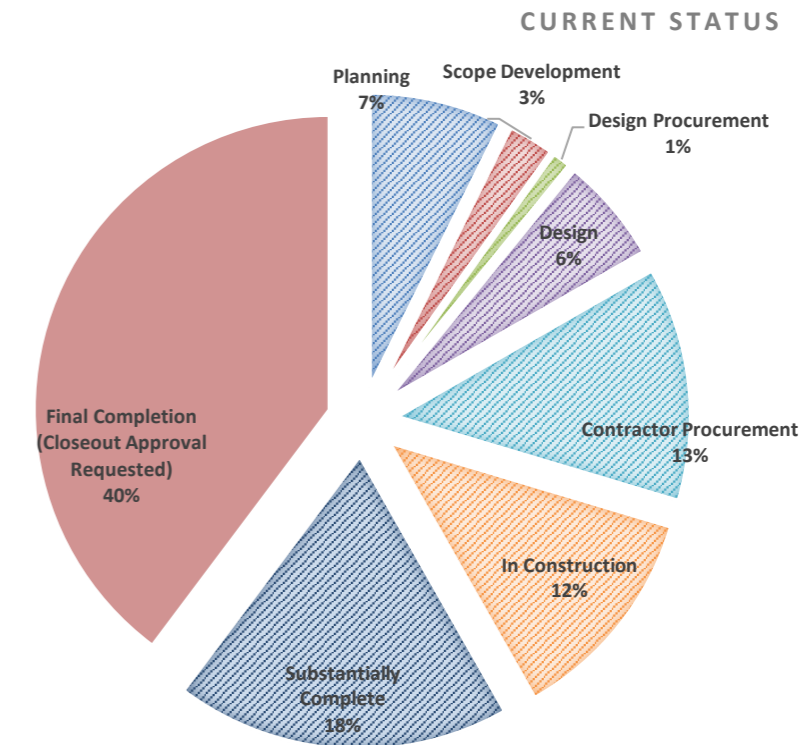

Active Projects By Type	#	Funding
Abatement	20	\$ 5,303,777.00
ADA Upgrades	7	\$ 1,737,977.00
Athletic Improvements	18	\$ 27,658,525.00
Building Repairs: Major/Emergency	8	\$ 13,957,141.01
Building Repairs: Minor	26	\$ 5,879,677.48
Central Garage & Transportation	3	\$ 535,700.00
Code Corrections	47	\$ 4,541,690.37
Emergency / Major Repair	0	\$ -
Exterior Door/Window Upgrades	15	\$ 20,087,657.58
IT Upgrades	4	\$ 102,631.50
Kitchen & Food Services	24	\$ 7,597,000.00
New Schools & Modernizations	17	\$ 670,722,865.00
Other	13	\$ 590,800.00
Parking Lots	19	\$ 5,634,046.00
Playgrounds	8	\$ 3,232,261.93
Renovations: Career Academy	10	\$ 14,372,000.00
Renovations: Classroom	2	\$ -
Renovations: Misc	8	\$ 28,984,859.00
Renovations: Staged	0	\$ -
Renovations: Pod Conversions	6	\$ 17,006,000.00
Security Upgrades	43	\$ 7,989,307.64
Systemic Upgrades: Electrical	4	\$ 7,126,222.00
Systemic Upgrades: HVAC	65	\$ 195,182,038.98
Systemic Upgrades: Life-Safety	4	\$ 620,000.00
Systemic Upgrades: Misc	24	\$ 53,471,912.00
TOTAL	395	\$ 1,092,334,089.49

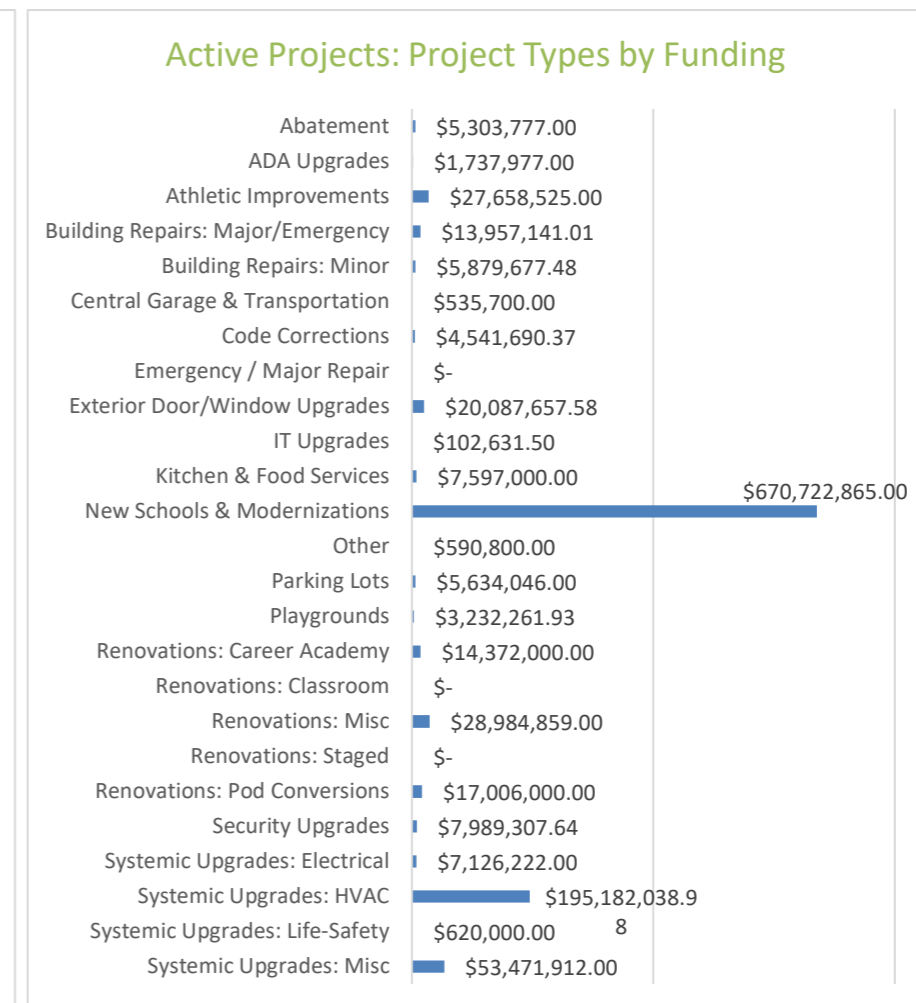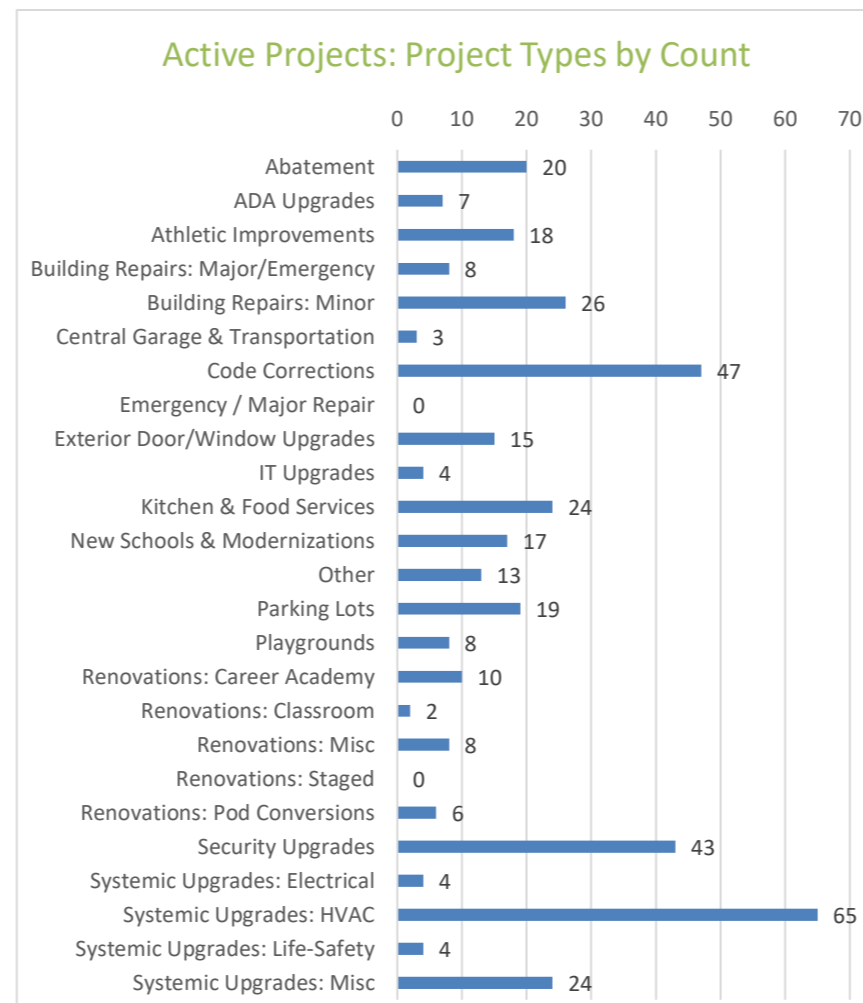

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
8	Allenwood ES	FY/17	State & County Funded	\$575,000	Exterior Door/Window Upgrades	Courtyard Windows Wall Replacement. A total of 49 windows and 7 doors will be replaced.	Final Completion (Closeout Approval Requested)	ricardo.garcia@pgcps.org	08/13/18	02/22/19	100%
7	Andrew Jackson Academy	FY/18	State & County Funded	\$17,641,000	Systemic Upgrades: HVAC	Replace 1971 HVAC equipment including one (1) chiller, 14 air handling units, heating and cooling piping, and the controls system, replace one (1) 1996 cooling tower, and replace two (2) 2000 steam boilers with hot water boilers.	Substantially Complete	henry2.lewis@pgcps.org	09/14/20	07/03/23	99%
7	Andrew Jackson Academy	FY/18	State & County Funded	\$639,000	Exterior Door/Window Upgrades	Window Replacement - All exterior windows throughout the building. The work consists of demolishing existing window system, removal of all related debris, and installation of 85 commercial grade aluminum single hung insulated window units	Substantially Complete	henry2.lewis@pgcps.org	09/01/20	08/20/22	99%
7	Andrew Jackson Academy	FY/21	County Funded	\$227,218	Security Upgrades	Install, program and test One hundred Eight IP Network Cameras (31- Outside, 77- Inside) with workstation and 43-inch Wall Mounted Live Viewing-Monitor	In Construction	george2.lacour@pgcps.org	04/16/21	06/30/21	
4	Annapolis Road Academy	FY/16	State & County Funded	\$890,000	Systemic Upgrades: HVAC	Steam and Condensate Piping Replacement	Final Completion (Closeout Approval Requested)	ricardo.garcia@pgcps.org	06/19/18	08/31/18	100%
4	Annapolis Road Academy	FY/16	State & County Funded	\$255,000	Systemic Upgrades: HVAC	Roof Top Unit Replacement	Substantially Complete	capital.programs@pgcps.org	06/19/18	08/31/18	95%
4	Annapolis Road Academy	FY/21	County Funded	\$525,000	Kitchen & Food Services	Kitchen Renovation: Remove existing kitchen equipment and replace/upgrade with new.	Substantially Complete	ricardo.garcia@pgcps.org	06/07/21	08/26/22	99%
8	Apple Grove ES	FY/22	County Funded	\$692,000	Systemic Upgrades: Misc	Roofing Replacement	Final Completion (Closeout Approval Requested)	ricardo.garcia@pgcps.org	08/25/23	08/03/24	100%
8	Apple Grove ES	FY/24	County Funded	\$250,000	Abatement	Asbestos Abatement	In Construction	alex.baylor@pgcps.org	06/10/24		
8	Apple Grove ES	FY/26	State & County Funded	\$2,357,000	Exterior Door/Window Upgrades	Replace the 1967 and 1998 windows and doors.	Planning	ricardo.garcia@pgcps.org			
8	Apple Grove ES	FY/26	County Funded	\$189,600	Code Corrections	Fire Alarm System Replacement	Design	pg_daniel.marks@pgcps.org	06/22/26	08/14/26	
4	Ardmore ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	06/20/16	02/15/17	100%
4	Ardmore ES	FY/26	County Funded	\$11,353	Building Repairs: Minor	Multipurpose Room Stage Flooring Refurbishment	Substantially Complete	pg_sean.mccoey@pgcps.org	05/18/26	05/19/26	98%

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
 May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
9	Baden ES	FY/14	State & County Funded	\$1,144,450	Systemic Upgrades: HVAC	Air Conditioning Initiative (ACI) - The request is to install a central air conditioning in the 1967 school building.	Substantially Complete	william5.smith@pgcps.org	06/14/17	09/29/17	99%
9	Baden ES	FY/17	State & County Funded	\$129,000	Exterior Door/Window Upgrades	Exterior Doors Replacement	Substantially Complete	henry2.lewis@pgcps.org		03/01/19	99%
4	Beacon Heights ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	06/20/16	08/20/21	100%
4	Beacon Heights ES	FY/17	State & County Funded	\$4,473,000	Systemic Upgrades: HVAC	AHUs, Condensate Piping, Metal Pan Ceiling & Univents Replacement	Substantially Complete	capital.programs@pgcps.org	06/17/19	08/21/19	95%
4	Beacon Heights ES	FY/26	State & County Funded	\$2,143,000	Systemic Upgrades: Misc	Replace the 1998 39,825 sf built-up roof.	Design Procurement	ricardo.garcia@pgcps.org			
4	Beacon Heights ES	FY/26	County Funded	\$175,000	Code Corrections	Fire Alarm System Replacement	Design	pg_daniel.marks@pgcps.org	09/21/26	12/18/26	
1	Beltsville Academy	FY/17	State & County Funded	\$2,811,000	Systemic Upgrades: HVAC	Univents & Controls and Window Replacement: 270 windows including tech fab panels will be replaced.	Substantially Complete	joseph.howell@pgcps.org	01/31/19	09/01/19	100%
1	Beltsville Academy	FY/18	State & County Funded	\$2,453,000	Systemic Upgrades: Misc	Roof Replacement - replace the entire 84,169 sf - 1991 built-up roof and 173 sf 1991 metal roof, including soffit and fascia at the music wing.	Substantially Complete	joseph.howell@pgcps.org	06/20/19	09/01/19	100%
1	Beltsville Academy	FY/24	Operating Funds	\$300,000	Abatement	Asbestos Abatement	Contractor Procurement	alex.baylor@pgcps.org	06/10/24		
1	Beltsville Academy		County Funded	\$2,341,310	Renovations: Misc	Provide (10) classroom modular additions	In Construction	joseph.howell@pgcps.org	09/01/22	08/15/23	100%
7	Benjamin Foulois K8	FY/23	Operating Funds	\$405,000	Systemic Upgrades: HVAC	Chiller Replacement	Substantially Complete	garth.deitzer@pgcps.org			
4	Benjamin Stoddert MS	FY/23	County Funded	\$800,000	Kitchen & Food Services	Kitchen Renovation	Substantially Complete	sunday.owolabi@pgcps.org			94%
4	Benjamin Stoddert MS	FY/26	State & County Funded	\$1,943,991	Systemic Upgrades: Misc	Replace the 1995 50,958 sf built-up roof	Contractor Procurement	diego.gonzalezguzman@pgcps.org		10/30/26	
5	Benjamin Tasker MS	FY/15	County Funded	\$60,000	Systemic Upgrades: Life-Safety	Code Corrections Fire Hydrant Project - This project consists of the replacement of the existing Fire Alarm System to meet current County, State and Federal building codes	Design Procurement	capital.programs@pgcps.org	06/19/17	09/30/17	0%
5	Benjamin Tasker MS	FY/17	State & County Funded	\$1,150,000	Systemic Upgrades: HVAC	Piping Replacement & Insulation: includes removal and replacement of all existing piping, steam traps and hangers on the dual distribution system. This will be Phase 1, which will consist of half of the school.	Final Completion (Closeout Approval Requested)	pg_rexie.fernando@pgcps.org	06/20/19	01/31/20	100%
5	Benjamin Tasker MS	FY/19	County Funded	\$216,524	Security Upgrades	Provide and install the following: 1. (98) Ninety-eight IP Network Cameras (24- Outside, 74- Inside) 2. 160TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing-Monitor PC with a 22" Monit	Final Completion (Closeout Approval Requested)	george2.lacour@pgcps.org	06/17/19	08/16/19	100%

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
 May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
5	Benjamin Tasker MS	FY/25	Grant Funded-ESSER	\$10,979,371	Renovations: Misc	Modular Addition	In Construction	joseph.howell@pgcps.org	02/03/26	02/05/27	35%
2	Berwyn Heights ES	FY/19	County Funded	\$107,444	Security Upgrades	Provide and install the following: 1. (41) Forty-nine IP Network Cameras (15- Outside, 26- Inside) 2. 90TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing-Monitor PC	Final Completion (Closeout Approval Requested)	george2.lacour@pgcps.org	07/08/19	11/30/19	100%
2	Berwyn Heights ES	FY/20	County Funded	\$2,000,000	Renovations: Misc	A phased limited renovation (Staged Renovation) of the facility.	Planning	ronald.skyles@pgcps.org			
4	Bladensburg ES	FY/16	County Funded	\$50,000	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is to be performed within the kitchen renovation project that is unable to be performed due to contractor's non-performance.	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	08/28/18	09/14/18	99%
4	Bladensburg ES	FY/16	County Funded	\$550,000	Kitchen & Food Services	Kitchen Renovation - This project includes the disconnection, removal, and dispose of the kitchen breaker panel (see note below), dishwasher, tables, dishwasher hood, booster heater, dish window, serving line, dish room wall, existing kitchen exhaust hood	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	04/16/18	08/23/19	99%
4	Bladensburg ES	FY/19	County Funded	\$119,820	Security Upgrades	Provide and install the following: 1. (49) Forty-nine IP Network Cameras (17- Outside, 32- Inside) 2. 90TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing-Monitor PC wit	Final Completion (Closeout Approval Requested)	george2.lacour@pgcps.org	06/03/19	07/19/19	100%
4	Bladensburg ES	FY/22	County Funded	\$3,305,513	Systemic Upgrades: HVAC	HVAC and Total Roof	Scope Development	capital.programs@pgcps.org			0%
4	Bladensburg ES	FY/22	County Funded	\$3,618,000	Systemic Upgrades: Misc	Roofing Replacement	Final Completion (Closeout Approval Requested)	ricardo.garcia@pgcps.org	04/09/24	06/04/24	100%
4	Bladensburg HS	FY/20	County Funded	\$5,300,000	Athletic Improvements	New Turf, Lighting and Running Track	Substantially Complete	william5.smith@pgcps.org	02/02/23	02/01/24	98%
4	Bonnie F. Johns Media Center	FY/21	County Funded	\$255,616	Security Upgrades	SANS server to for sixty-five IP camera systems located throughout the county.	In Construction	george2.lacour@pgcps.org	03/15/21	04/30/21	
5	Bowie HS	FY/15	County Funded	\$135,000	ADA Upgrades	Misc. ADA Improvements	Substantially Complete	henry2.lewis@pgcps.org	06/24/15	08/15/16	98%
5	Bowie HS	FY/17	State & County Funded	\$2,556,000	Abatement	Fireproofing for Air Conditioning Piping Replacement: includes the removal of asbestos containing encapsulated sprayed applied fireproofing, pipe insulation and associated mudded fittings.	Final Completion (Closeout Approval Requested)	joseph.howell@pgcps.org	06/27/18	09/03/18	100%
5	Bowie HS	FY/22	County Funded	\$54,000	Systemic Upgrades: Misc	Roof Replacement	Planning	anoop.gupta@pgcps.org			
5	Bowie HS	FY/25	County Funded	\$34,240	Building Repairs: Minor	Gym Fan Installation	Substantially Complete	diego.gonzalezguzman@pgcps.org	09/20/25	11/14/25	100%

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
 May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
5	Bowie HS Annex	FY/16	State & County Funded	\$25,865,000	New Schools & Modernizations	Limited Renovation - Limited renovation and improvements to the existing special education program. Includes five major systemic projects in addition to selected educational program enhancements and systemic renovations.	In Construction	hiwot.haileselassie@pgcps.org	12/19/19	04/29/22	97%
5	Bowie HS Annex	FY/18	County Funded	\$450,000	Kitchen & Food Services	Replace kitchen exhaust system. Create opening in exterior wall for combination walk-in refrigerator and freezer. Provide and install one double convection oven, one two compartment steamer.	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	06/16/19	08/16/19	100%
7	Bradbury Heights ES	FY/17	State & County Funded	\$1,719,000	Systemic Upgrades: Misc	Roof Replacement: includes replacing 50,025 sq. ft. of roof.	Final Completion (Closeout Approval Requested)	william5.smith@pgcps.org	07/09/18	10/05/18	100%
7	Bradbury Heights ES	FY/26	County Funded	\$400,000	Systemic Upgrades: Life-Safety	Structural Concern - Retaining Wall	Scope Development	pg_daniel.marks@pgcps.org	06/22/26	08/14/26	
3	Buck Lodge MS	FY/16	State & County Funded	\$2,186,000	Systemic Upgrades: HVAC	Unit Ventilator and Exhaust Fans Replacement	Substantially Complete	ricardo.garcia@pgcps.org	06/19/18	08/31/18	95%
3	Buck Lodge MS	FY/19	County Funded	\$198,700	Security Upgrades	Provide and install the following: 1. (87) Eighty-seven IP Network Cameras (23- Outside, 64- Inside) 2. 130TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing-Monitor PC	Final Completion (Closeout Approval Requested)	george2.lacour@pgcps.org	06/03/19	07/15/19	100%
3	Buck Lodge MS	FY/24	County Funded	\$35,660	Building Repairs: Minor	Gym - Flooring Refurbishment	Substantially Complete	pg_daniel.marks@pgcps.org	07/24/24		95%
3	Buck Lodge MS	FY/24	County Funded		Building Repairs: Minor	Locker Replacement	Final Completion (Closeout Approval Requested)	pg_keelan.hendricks@pgcps.org	06/18/24	08/27/24	100%
5	C. Elizabeth Reig Special Center	FY/16	State & County Funded	\$8,752,876	New Schools & Modernizations	Limited Renovation - Limited renovation and improvements to the existing special education program. Includes five major systemic projects in addition to selected educational program enhancements and systemic renovations.	Substantially Complete	hiwot.haileselassie@pgcps.org	12/19/19	10/03/23	98%
1	Calverton ES	FY/12	County Funded	\$500,000	Kitchen & Food Services	Kitchen Renovation - Expand kitchen to allow installation of one additional serving line, walk-in freezer and walk-in refrigerator. Replace kitchen exhaust system. Install elevator to deliver food to the second floor.	Substantially Complete	joseph.howell@pgcps.org	06/19/17	08/01/17	100%
1	Calverton ES	FY/20	County Funded		New Schools & Modernizations	Phased limited renovation (Staged Renovation) of the facility including an addition	Design	ricardo.garcia@pgcps.org			

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
 May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
6	Capitol Heights ES	FY/22	County Funded	\$478,308	Systemic Upgrades: HVAC	Chiller Replacement	Final Completion (Closeout Approval Requested)	pg_sean.mccoy@pgcps.org	01/20/24	08/30/24	100%
6	Capitol Heights ES	FY/23	County Funded	\$400,000	Kitchen & Food Services	Kitchen & Food Services Renovation	Design	ricardo.garcia@pgcps.org	06/29/26		
6	Capitol Heights ES	FY/26	County Funded		Abatement	Asbestos Removal	Final Completion (Closeout Approval Requested)	alex.baylor@pgcps.org	08/13/25	10/21/25	100%
6	Capitol Heights ES	FY/26	County Funded		Abatement	Asbestos - Reinstall Flooring	Final Completion (Closeout Approval Requested)	alex.baylor@pgcps.org	08/28/25	10/21/25	100%
6	Carmody Hills ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	06/20/16	01/27/17	99%
6	Carmody Hills ES	FY/21	County Funded	\$200,000	Security Upgrades	New IP camera system	Design	george2.lacour@pgcps.org			
3	Carole Highlands ES	FY/20	County Funded	\$114,527	Security Upgrades	Provide and install the following: 1. (43) Forty-nine IP Network Cameras (19- Outside, 24- Inside) 2. 90TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor	Final Completion (Closeout Approval Requested)	george2.lacour@pgcps.org	08/03/20	08/31/20	100%
2	Carrollton ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	06/20/16	08/12/16	99%
1	Catherine T. Reed ES	FY/19	County Funded	\$25,000	Kitchen & Food Services	Remove and Replace (1) New Serving Line	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	10/01/20	02/26/21	100%
1	Catherine T. Reed ES	FY/24	Operating Funds	\$200,000	Abatement	Asbestos Abatement	Contractor Procurement	alex.baylor@pgcps.org	06/10/24		
6	Central HS	FY/18	State & County Funded	\$20,218,000	Systemic Upgrades: HVAC	Replace the entire 1982 heating and ventilating system with a complete heating, ventilating and air conditioning system, including boilers, chiller, rooftop units, air handling units, terminal units, piping, and controls.	Final Completion (Closeout Approval Requested)	anoop.gupta@pgcps.org	06/24/22	08/26/22	100%
3	Cesar Chavez ES	FY/21	County Funded	\$200,000	Security Upgrades	New IP camera system	Design	george2.lacour@pgcps.org			
3	Cesar Chavez ES	FY/21	County Funded	\$444,557	Systemic Upgrades: HVAC	Boilers, 2-MPR AHUs, Water Heater, Controls in Plant Replacement	In Construction	pg_sean.mccoy@pgcps.org	10/01/23	08/16/24	98%

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
 May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
3	Cesar Chavez ES	FY/23	County Funded	\$434,134	Systemic Upgrades: HVAC	Chiller Replacement	In Construction	pg_sean.mccoy@pgcps.org	11/01/24	01/31/25	98%
2	Charles Carroll MS	FY/19	County Funded	\$50,000	Kitchen & Food Services	Remove and Replace (2) New Serving Lines	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	10/01/20	02/26/21	100%
4	Charles Herbert Flowers HS	FY/15	County Funded	\$199,000	Renovations: Career Academy	Secondary School Reform (SSR) - Renovations for the academies of Science & Technology and Engineering & Science	Substantially Complete	henry2.lewis@pgcps.org	06/15/17	08/10/17	98%
4	Charles Herbert Flowers HS	FY/16	County Funded	\$38,000	Renovations: Career Academy	Secondary School Reform (SSR) - Renovations for the academy of Business and Finance.	Substantially Complete	henry2.lewis@pgcps.org	06/15/17	08/10/17	98%
4	Charles Herbert Flowers HS	FY/19	County Funded	\$439,153	Security Upgrades	Provide and install the following: 1. (214) Two Hundred and Fourteen IP Network Cameras (38- Outside, 176- Inside) 2. (2) 160TB Storage Servers RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing-Monitor	Final Completion (Closeout Approval Requested)	george2.lacour@pgcps.org	01/01/20	04/01/20	100%
4	Charles Herbert Flowers HS	FY/19	County Funded	\$75,000	Kitchen & Food Services	Remove and Replace (3) New Serving Lines	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	10/01/20	02/26/21	100%
4	Charles Herbert Flowers HS	FY/21	State & County Funded	\$11,168,241	Systemic Upgrades: HVAC	Partial funding to replace the 1999 HVAC system and roof replacement.	In Construction	sunday.owolabi@pgcps.org	12/23/24		65%
4	Charles Herbert Flowers HS	FY/23	State & County Funded	\$12,483,000	Systemic Upgrades: HVAC	HVAC-Roof Replacement	In Construction	sunday.owolabi@pgcps.org			
4	Charles Herbert Flowers HS	FY/25	State-HSFF Funded	\$2,905,391	Systemic Upgrades: Misc	Roof Replacement (HSFF)	Scope Development	sunday.owolabi@pgcps.org			
4	Charles Herbert Flowers HS	FY/26	County Funded	\$1,500,000	Systemic Upgrades: HVAC	Three (3) chillers, two (2) air cooled condensers, and cooling tower replacement	Scope Development	sunday.owolabi@pgcps.org	06/22/26	08/14/26	
4	Charles Herbert Flowers HS	FY/26	County Funded	\$500,000	Systemic Upgrades: HVAC	Boiler Modernization	Scope Development	sunday.owolabi@pgcps.org	06/22/26	08/14/26	
3	Cherokee Lane ES	FY/20	State & County Funded	\$64,375,255	New Schools & Modernizations	Replacement facility to be co-located on Buck Lodge MS site. Expansion from 400 to 800 seats to relieve over enrollment in the Adelphi Area.	Substantially Complete	joseph.howell@pgcps.org	08/03/20	04/15/22	99%
3	Chillum ES	FY/20	State & County Funded	\$2,558,000	Renovations: Pod Conversions	Convert existing open space pods into conventional classrooms.	Final Completion (Closeout Approval Requested)	ricardo.garcia@pgcps.org	06/01/22	09/01/23	100%
3	Chillum ES	FY/21	County Funded	\$200,000	Security Upgrades	New IP camera system	Design	george2.lacour@pgcps.org			
3	Chillum ES	FY/26	State & County Funded	\$2,596,000	Exterior Door/Window Upgrades	Replace the 1978 windows and exterior doors.	Planning	ricardo.garcia@pgcps.org			

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
9	Clinton Grove ES	FY/24	County Funded	\$275,000	Code Corrections	Fire Alarm System Replacement	Final Completion (Closeout Approval Requested)	pg_daniel.marks@pgcps.org	06/30/25	01/14/26	100%
9	Clinton Grove ES	FY/26	County Funded	\$777,000	Systemic Upgrades: Electrical	Switchgear Replacement	Contractor Procurement	pg_sean.mccoy@pgcps.org	07/06/26	08/21/26	
4	Columbia Park ES	FY/17	State & County Funded	\$592,000	Systemic Upgrades: HVAC	Univent Replacement: Along with steam heat unit ventilators conversion.	Final Completion (Closeout Approval Requested)	kmuse@pgcps.org	06/14/19	01/31/22	100%
6	Concord ES	FY/21	County Funded	\$200,000	Security Upgrades	New IP camera system	Design	george2.lacour@pgcps.org			
3	Cool Spring ES	FY/24	State & County Funded	\$95,774,000	New Schools & Modernizations	Construction of a new school in front of the existing Cool Spring Elementary School while the existing school is in operation. The proposed school, including the Judy Center is anticipated to be three floors and accommodate 900 students. The new school will be built to be energy efficient and meet all current building and accessibility codes.	Design	joseph.howell@pgcps.org			0%
4	Cooper Lane ES	FY/26	State & County Funded	\$1,774,000	Exterior Door/Window Upgrades	Replace the 1962/1963/1966/1993 windows and exterior doors	Planning	ricardo.garcia@pgcps.org			
6	Cora L. Rice ES	FY/24	State-ASP Funded	\$335,000	Building Repairs: Minor	Public Address System and Clocks Replacement	Final Completion (Closeout Approval Requested)	pg_daniel.marks@pgcps.org	06/17/24	08/16/24	100%
6	Cora L. Rice ES	FY/26	County Funded	\$262,942	Systemic Upgrades: Electrical	PA System - Wiring and Speaker Replacement	In Construction	pg_daniel.marks@pgcps.org	02/02/26	08/14/26	
8	Crossland HS	FY/16	County Funded	\$27,553	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	07/17/19	08/16/19	100%
8	Crossland HS	FY/19	County Funded	\$75,000	Kitchen & Food Services	Remove and Replace (3) New Serving Lines	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	10/01/20	02/26/21	100%
8	Crossland HS	FY/23	State-ASP Funded	\$2,641,399	Athletic Improvements	Bleacher/Press-Box Replacement	Final Completion (Closeout Approval Requested)	ricardo.garcia@pgcps.org	05/20/24	09/11/24	100%
8	Crossland HS	FY/24	County Funded	\$192,263	Building Repairs: Minor	Gym - Flooring Replacement	Substantially Complete	pg_daniel.marks@pgcps.org	05/29/24		100%
8	Crossland HS	FY/25	County Funded	\$763,000	Athletic Improvements	Stadium Lighting Installation	Planning	ricardo.garcia@pgcps.org	06/22/26	09/02/26	

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
 May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
1	Deerfield Run ES	FY/22	County Funded	\$505,002	Systemic Upgrades: HVAC	Chiller Replacement	Final Completion (Closeout Approval Requested)	pg_sean.mccoy@pgcps.org	03/04/24	08/30/24	100%
7	District Heights ES	FY/15	County Funded	\$400,000	Kitchen & Food Services	Replace Exhaust System & Walk-in Refrigerator and Add Walk-in Freezer and Combination Oven.	Substantially Complete	joseph.howell@pgcps.org	06/27/18	09/01/18	100%
7	District Heights ES	FY/16	County Funded	\$36,735	Abatement	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	06/20/16	08/09/16	100%
7	District Heights ES	FY/16	County Funded	\$125,000	Kitchen & Food Services	Kitchen Renovation - This project includes the disconnection, removal, and disposal of the dishwasher, dishwasher hood, dishwasher tables, booster heater and create opening in wall to allow access to new walk-in freezer.	Final Completion (Closeout Approval Requested)	joseph.howell@pgcps.org	09/20/17	10/31/17	100%
7	District Heights ES	FY/17	State & County Funded	\$255,000	Systemic Upgrades: HVAC	Roof Top Units (RTUs) Replacement: includes replacing 2 existing roof mount units with high efficiency HVAC units with variable speed frequency drives.	Final Completion (Closeout Approval Requested)	joseph.howell@pgcps.org	05/01/17	07/10/17	100%
7	District Heights ES	FY/18	County Funded	\$2,442,999	Building Repairs: Major/Emergency	Limited Renovations (Interior Architectural) Phase I	Final Completion (Closeout Approval Requested)	joseph.howell@pgcps.org	04/08/19	09/03/19	100%
7	District Heights ES	FY/18	County Funded	\$1,819,369	Building Repairs: Major/Emergency	Modular Classrooms & Asbestos Remediation Phase II	Final Completion (Closeout Approval Requested)	joseph.howell@pgcps.org	03/18/19	09/03/19	100%
7	District Heights ES	FY/19	County Funded	\$2,991,451	Systemic Upgrades: HVAC	AC Upgrades Phase I	Final Completion (Closeout Approval Requested)	joseph.howell@pgcps.org	04/08/19	09/03/19	100%
7	District Heights ES	FY/22	County Funded	\$27,000	Kitchen & Food Services	Serving Line Replacement	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	08/08/23	08/12/23	100%
7	District Heights ES	FY/26	State-ASP Funded	\$207,698	Parking Lots	Parking Lot Replacement	Contractor Procurement	pg_sean.mccoy@pgcps.org	07/21/26	07/30/26	
4	Dodge Park ES	FY/26	State-ASP Funded	\$130,095	Playgrounds	Playground Replacement	Contractor Procurement	pg_daniel.marks@pgcps.org	06/29/26	09/29/26	
7	Drew Freeman MS	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	06/20/16	08/10/16	100%

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
 May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
7	Drew Freeman MS	FY/16	State & County Funded	\$2,783,000	Systemic Upgrades: HVAC	Unit Ventilator, Exhaust Fans & AHUs Replacement	Substantially Complete	capital.programs@pgcps.org	06/19/18	08/31/18	95%
7	Drew Freeman MS	FY/16	State & County Funded	\$5,977,000	Systemic Upgrades: Electrical	Lighting and Wiring Replacement	Substantially Complete	capital.programs@pgcps.org	06/19/18	08/31/18	95%
1	DuVal HS	FY/14	County Funded	\$821,000	Renovations: Career Academy	Secondary School Reform (SSR) - Renovations for the academies of Consumer Sciences, Hospitality: Tourism, Engineering & Science and Graphics, Arts, Media and Communications (Priority 63).	Substantially Complete	henry2.lewis@pgcps.org	06/15/17	08/22/17	98%
1	DuVal HS	FY/17	State & County Funded	\$2,556,000	Exterior Door/Window Upgrades	Window Replacement: total of 655 windows to be replaced. Include demolishing existing window system, removal of all related debris and the installation of heavy commercial grade single hung aluminum windows with double insulated units.	Substantially Complete	henry2.lewis@pgcps.org	06/19/19	08/02/21	98%
1	DuVal HS	FY/22	County Funded	\$1,500,000	Systemic Upgrades: HVAC	Main Bldg. - 2 RTUs, Fan Coil, Controls Annex - Cafeteria RTU, 5 RTU	Final Completion (Closeout Approval Requested)	pg_sean.mccoy@pgcps.org	06/27/22	09/30/24	100%
1	DuVal HS	FY/24	County Funded	\$82,761	ADA Upgrades	Lift Replacement (Stage)	Final Completion (Closeout Approval Requested)	pg_daniel.marks@pgcps.org	06/17/24	11/01/24	100%
1	DuVal HS	FY/24	Operating Funds	\$300,000	Abatement	Asbestos Abatement	In Construction	alex.baylor@pgcps.org	06/20/24	08/11/24	100%
1	DuVal HS	FY/25	State-ASP Funded	\$1,209,426	Athletic Improvements	Football Stadium Bleachers & Press-box Replacement.	Planning	diego.gonzalezguzman@pgcps.org	06/22/26	09/02/26	
1	Dwight Eisenhower MS	FY/17	State & County Funded	\$384,000	Exterior Door/Window Upgrades	Storefront Replacement: includes demo, abatement and replacement of existing exterior storefront doors and windows with new aluminum system.	Final Completion (Closeout Approval Requested)	ricardo.garcia@pgcps.org	08/13/18	02/22/19	100%
1	Dwight Eisenhower MS	FY/19	State & County Funded	\$12,063,600	Systemic Upgrades: HVAC	HVAC & Building Envelope / Replace the 1969-1974 central controls system, HVAC piping, all ten (10) AHUs, 45 finned tube radiators, four (4) self-contained unit ventilators, 17 floor mounted fan coil units, two (2) ceiling mounted AHUs, chiller	Contractor Procurement	anoop.gupta@pgcps.org	06/07/21	08/18/25	48%
1	Dwight Eisenhower MS	FY/20	County Funded	\$296,584	Security Upgrades	Provide and install the following: 1. (132) One Hundred Thirty-two IP Network Cameras (45- Outside, 87- Inside) 2. 170TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing	Final Completion (Closeout Approval Requested)	george2.lacour@pgcps.org	03/10/20	07/31/20	100%
1	Dwight Eisenhower MS	FY/26	County Funded	\$21,435	Building Repairs: Minor	Dance Studio Flooring Replacement	Substantially Complete	pg_sean.mccoy@pgcps.org	05/13/26	05/14/26	98%
1	Dwight Eisenhower MS	FY/26	State-ASP Funded	\$350,000	Parking Lots	Parking Lot Refurbishment	Contractor Procurement	pg_sean.mccoy@pgcps.org	06/22/26	07/06/26	

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
2	Eleanor Roosevelt HS	FY/15	State & County Funded	\$903,000	Renovations: Pod Conversions	Open Space Pod Conversion Renovations / 1 Pod-(6 classrooms). Project required to remove the temporary partitions and replace them with permanent partitions.	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	06/15/18	09/02/18	100%
2	Eleanor Roosevelt HS	FY/15	County Funded	\$300,000	Parking Lots	Major Repairs Driveways, Parking Lots & Entrance Project	Design	capital.programs@pgcps.org	06/19/17	03/30/19	0%
2	Eleanor Roosevelt HS	FY/15	County Funded	\$102,000	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements	Substantially Complete	sunday.owolabi@pgcps.org	06/23/15	08/19/15	99%
4	Ellen Ochoa MS (former New Glenridge Area MS)	FY/20	State & County Funded	\$80,145,734	New Schools & Modernizations	New Middle School to be built in the Glenridge area	In Construction	hiwot.haileselassie@pgcps.org	12/27/21	05/01/24	99%
6	Ernest Everett Just MS	FY/20	County Funded	\$274,108	Security Upgrades	Provide and install the following: 1. (119) One Hundred Nineteen IP Network Cameras (40-Outside, 79- Inside) 2. 170TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing	Final Completion (Closeout Approval Requested)	george2.lacour@pgcps.org	06/29/20	10/31/20	100%
6	Ernest Everett Just MS	FY/26	County Funded	\$1,000,000	Systemic Upgrades: HVAC	Controls Replacement	Contractor Procurement	pg_sean.mccoy@pgcps.org	06/22/26	01/08/27	
9	Eugene Burroughs MS / Accokeek Academy	FY/19	County Funded	\$12,546	Security Upgrades	Install card access on three door 6,7 and 8	Final Completion (Closeout Approval Requested)	george2.lacour@pgcps.org	07/13/20	12/04/20	100%
9	Eugene Burroughs MS / Accokeek Academy	FY/20	County Funded	\$94,518	Security Upgrades	Upgrade camera system head end equipment to Genetec.	Final Completion (Closeout Approval Requested)	george2.lacour@pgcps.org	02/14/20	06/30/20	100%
9	Facilities Administration Building	FY/21	County Funded	\$8,000,000	Building Repairs: Major/Emergency	HVAC and Architectural Finishes	In Construction	joseph.howell@pgcps.org	09/07/22	09/01/23	99%
9	Facilities Administration Building	FY/21	County Funded	\$61,042	Abatement	Asbestos Abatement	Substantially Complete	joseph.howell@pgcps.org	12/16/19	01/03/20	100%
9	Facilities Service Base	FY/24	County Funded	\$109,280	Systemic Upgrades: Electrical	Generator Replacement	Final Completion (Closeout Approval Requested)	pg_keelan.hendricks@pgcps.org	12/20/24		100%
4	Fairmont Heights HS (Replacement)	FY/12	State & County Funded	\$79,912,000	New Schools & Modernizations	Facility Replacement - This project will deliver a state-of-the-art new facility designed for a State Rated Capacity of 953 students on a 38.7-acre site with an overall sq. ft. of 190,058.	Substantially Complete	nadine.belizaire@pgcps.org	09/15/15	12/31/21	97%

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
 May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
4	Fairmont Heights HS (Replacement)	FY/16	State & County Funded	\$14,665,000	New Schools & Modernizations	Facility Replacement - This project will deliver a state-of-the-art new facility designed for a State Rated Capacity of 953 students on a 38.7-acre site with an overall sq. ft. of 190,058.	Substantially Complete	nadine.belizaire@pgcps.org	09/15/15	12/31/21	97%
4	Fairmont Heights HS (Replacement)	FY/20	County Funded	\$563,536	Athletic Improvements	Scoreboard Installation for Football, Baseball and Softball Fields	Final Completion (Closeout Approval Requested)	ricardo.garcia@pgcps.org	07/24/23	11/20/24	100%
8	Flintstone ES	FY/17	State & County Funded	\$1,213,000	Systemic Upgrades: HVAC	Piping Replacement: includes removal and replacement of all existing steam supply and return piping, steam traps, satellite condensate tanks, pipe supports on the dual pipe distribution system.	Substantially Complete	william5.smith@pgcps.org	06/01/19	08/15/19	95%
8	Flintstone ES	FY/24	County Funded	\$175,000	Parking Lots	Parking Lot Refurbishment	Final Completion (Closeout Approval Requested)	pg_daniel.marks@pgcps.org	06/17/24	08/09/24	100%
8	Flintstone ES	FY/25	County Funded	\$817,496	Building Repairs: Major/Emergency	Exterior Wall Replacement	In Construction	pg_daniel.marks@pgcps.org	06/22/26	08/14/26	
8	Forest Heights ES	FY/15	County Funded	\$45,000	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	06/23/15	08/19/15	100%
8	Forest Heights ES	FY/18	County-Rosecroft Funded	\$34,211	IT Upgrades	Electronic Sign (FY18 Rosecroft Funds \$9,210.52; FY20 Rosecroft Funds \$25,000)	Final Completion (Closeout Approval Requested)	pg_rexie.fernando@pgcps.org	02/15/21	06/20/21	100%
8	Forest Heights ES	FY/24	State-HSFF Funded	\$1,859,000	Systemic Upgrades: Misc	Roof Replacement (HSFF)	Final Completion (Closeout Approval Requested)	ricardo.garcia@pgcps.org	03/28/25	10/29/25	100%
7	Forestville HS	FY/16	State & County Funded	\$753,000	Systemic Upgrades: Misc	Final Phase Roof Replacement - The scope of this project will be to remove and replace approximately 21,600 sf of the 1965 section of this building and approximately 1,200 of the 1993 additions to the 1965 building.	Substantially Complete	cfloeck@pgcps.org	06/15/18	10/30/18	98%
7	Forestville HS	FY/26	Operating Funds	\$1,434,701	Systemic Upgrades: HVAC	Controls Upgrade	In Construction	jason.walker@pgcps.org			
8	Fort Foote ES	FY/18	County-Rosecroft Funded	\$34,211	IT Upgrades	Electronic Sign (FY18 Rosecroft Funds \$9,210.52; FY20 Rosecroft Funds \$25,000)	Final Completion (Closeout Approval Requested)	pg_rexie.fernando@pgcps.org	02/15/21	06/20/21	100%

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
 May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
8	Fort Foote ES	FY/21	County Funded	\$93,243	Security Upgrades	Install, program and test Forty IP Network Cameras (18- Outside, 22- Inside) with workstation and 43-inch Wall Mounted Live Viewing-Monitor	In Construction	george2.lacour@pgcps.org	05/17/21	06/30/21	
8	Fort Foote ES	FY/26	State-HSFF Funded	\$1,792,174	Systemic Upgrades: Misc	Replacement of approximately 49,000 sf of roof installed in 2004. This is a full roof replacement.	Design Procurement	ricardo.garcia@pgcps.org			
8	Fort Foote ES	FY/26	State-ASP Funded	\$423,565	Playgrounds	Playground Replacement	Contractor Procurement	pg_daniel.marks@pgcps.org	06/22/26	08/14/26	
9	Fort Washington Forest ES	FY/19	County Funded	\$25,000	Kitchen & Food Services	Remove and Replace (1) New Serving Line	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	10/01/20	02/26/21	100%
1	Frances Fuchs ECC	FY/26	County Funded	\$200,000	Code Corrections	Fire Alarm System Replacement	In Construction	pg_daniel.marks@pgcps.org	06/22/26	08/14/26	
1	Frances Fuchs ECC	FY/26	State-ASP Funded	\$785,791	Playgrounds	Playground Replacement	Contractor Procurement	pg_daniel.marks@pgcps.org	06/30/26	09/29/26	
6	Francis Scott Key ES	FY/19	County Funded	\$129,769	Security Upgrades	Provide and install the following: 1. (51) Forty-nine IP Network Cameras (18- Outside, 33- Inside) 2. 110TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing-Monitor PC	Final Completion (Closeout Approval Requested)	george2.lacour@pgcps.org	09/01/19		100%
6	Francis Scott Key ES	FY/19	County Funded	\$129,769	Security Upgrades	Provide and install the following: 1. (51) Forty-nine IP Network Cameras (18- Outside, 33- Inside) 2. 110TB (useable) TB Storage Server RAID 5 3. UPS for	Final Completion (Closeout Approval)	george2.lacour@pgcps.org	09/01/19		100%
9	Francis T. Evans ES	FY/15	State & County Funded	\$3,234,000	Renovations: Pod Conversions	Phase I - Open Space Pod Conversion Renovations / 3 Pods	Substantially Complete	cfloeck@pgcps.org	06/15/18	09/30/18	98%
9	Francis T. Evans ES	FY/15	State & County Funded	\$3,234,000	Renovations: Pod Conversions	Phase I - Open Space Pod Conversion Renovations / 3 Pods	Substantially Complete	cfloeck@pgcps.org	06/15/18	09/30/18	98%
9	Francis T. Evans ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-	Final Completion (Closeout)	sunday.owolabi@pgcps.org	06/20/16	09/19/16	100%
9	Francis T. Evans ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-	Final Completion (Closeout)	sunday.owolabi@pgcps.org	06/20/16	09/19/16	100%
9	Francis T. Evans ES	FY/26	County Funded	\$443,850	Playgrounds	Playground Replacement	In Construction	pg_daniel.marks@pgcps.org	06/22/26	03/12/27	
9	Francis T. Evans ES	FY/26	County Funded	\$443,850	Playgrounds	Playground Replacement	In Construction	pg_daniel.marks@pgcps.org	06/22/26	03/12/27	

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
 May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
9	Frederick Douglass HS	FY/22	County Funded	\$9,000,000	Athletic Improvements	Football Stadium Renovation	In Construction	diego.gonzalezguzman@pgcps.org	05/12/25	08/31/26	85%
9	Frederick Douglass HS	FY/22	County Funded	\$9,000,000	Athletic Improvements	Football Stadium Renovation	In Construction	diego.gonzalezguzman@pgcps.org	05/12/25	08/31/26	85%
9	Frederick Douglass HS	FY/25	County Funded	\$64,200	Building Repairs: Minor	Gym Fan Installation	Substantially Complete	diego.gonzalezguzman@pgcps.org	10/06/25	10/10/25	100%
9	Frederick Douglass HS	FY/25	County Funded	\$64,200	Building Repairs: Minor	Gym Fan Installation	Substantially Complete	diego.gonzalezguzman@pgcps.org	10/06/25	10/10/25	100%
8	Friendly HS	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current	Final Completion (Closeout Approval)	sunday.owolabi@pgcps.org	06/20/16	08/10/16	100%
8	Friendly HS	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	06/20/16	08/10/16	100%
8	Friendly HS	FY/23	County Funded	\$237,760	Building Repairs: Minor	Tennis Court Replacement	Final Completion (Closeout)	pg_daniel.marks@pgcps.org	06/19/23	08/18/23	100%
8	Friendly HS	FY/23	County Funded	\$604,450	Building Repairs: Minor	Running Track Upgrade	Final Completion (Closeout Approval Requested)	pg_daniel.marks@pgcps.org	06/19/23	08/18/23	100%
8	Friendly HS	FY/23	County Funded	\$237,760	Building Repairs: Minor	Tennis Court Replacement	Final Completion (Closeout Approval Requested)	pg_daniel.marks@pgcps.org	06/19/23	08/18/23	100%
8	Friendly HS	FY/23	County Funded	\$604,450	Building Repairs: Minor	Running Track Upgrade	Final Completion (Closeout Approval Requested)	pg_daniel.marks@pgcps.org	06/19/23	08/18/23	100%
8	Friendly HS	FY/24	County Funded	\$47,044	Building Repairs: Minor	Corridor and Locker Room Locker Replacement	Final Completion (Closeout Approval Requested)	pg_keelan.hendricks@pgcps.org	06/15/24	06/24/24	100%
8	Friendly HS	FY/24	County Funded	\$47,044	Building Repairs: Minor	Corridor and Locker Room Locker Replacement	Final Completion (Closeout Approval Requested)	pg_keelan.hendricks@pgcps.org	06/15/24	06/24/24	100%

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
 May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
6	G. James Gholson MS	FY/21	County Funded	\$400,000	Security Upgrades	New IP camera system	Design	george2.lacour@pgcps.org			
6	G. James Gholson MS	FY/21	County Funded	\$400,000	Security Upgrades	New IP camera system	Design	george2.lacour@pgcps.org			
4	Gaywood ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current	Final Completion (Closeout Approval)	sunday.owolabi@pgcps.org	06/20/16	08/10/16	100%
4	Gaywood ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-	Final Completion (Closeout)	sunday.owolabi@pgcps.org	06/20/16	08/10/16	100%
4	Gaywood ES	FY/17	State & County Funded	\$831,000	Systemic Upgrades: HVAC	Univent Replacement: includes replacing 29, 1958 classroom steam heat unit ventilators with 8 radiator and 8 fan coil units.	Substantially Complete	william5.smith@pgcps.org	06/21/18	08/20/18	99%
4	Gaywood ES	FY/17	State & County Funded	\$831,000	Systemic Upgrades: HVAC	Univent Replacement: includes replacing 29, 1958 classroom steam heat unit ventilators with 8	Substantially Complete	william5.smith@pgcps.org	06/21/18	08/20/18	99%
4	Gaywood ES	FY/18	County Funded	\$350,000	Kitchen & Food Services	Remove roll-down door and close opening. Remove dishwasher hood. Add combination walk-in	Final Completion (Closeout)	sunday.owolabi@pgcps.org	07/15/19	08/28/19	99%
4	Gaywood ES	FY/18	County Funded	\$350,000	Kitchen & Food Services	Remove roll-down door and close opening. Remove dishwasher hood. Add combination walk-in refrigerator & freezer.	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	07/15/19	08/28/19	99%
4	Gaywood ES	FY/24	County Funded	\$250,000	Abatement	Asbestos Abatement	Contractor Procurement	alex.baylor@pgcps.org	06/20/24		20%
4	Gaywood ES	FY/24	County Funded	\$250,000	Abatement	Asbestos Abatement	Contractor Procurement	alex.baylor@pgcps.org	06/20/24		20%
4	Glenn Dale ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	06/20/16	08/12/16	100%
4	Glenn Dale ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	06/20/16	08/12/16	100%

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
 May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
2	Greenbelt ES	FY/17	State & County Funded	\$1,214,000	Systemic Upgrades: HVAC	Chiller Replacement & HVAC Controls Upgrade: includes removing two 1993, 120 ton air cooled Trane chillers.	Final Completion (Closeout Approval Requested)	pg_rexie.fernando@pgcps.org	06/25/18	08/24/18	100%
2	Greenbelt ES	FY/17	State & County Funded	\$1,214,000	Systemic Upgrades: HVAC	Chiller Replacement & HVAC Controls Upgrade: includes removing two 1993, 120 ton air cooled Trane chillers.	Final Completion (Closeout Approval Requested)	pg_rexie.fernando@pgcps.org	06/25/18	08/24/18	100%
2	Greenbelt ES	FY/20	County Funded	\$148,662	Security Upgrades	Provide and install the following: 1. (58) Fifty-eight IP Network Cameras (24- Outside, 35- Inside) 2. 110TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing	Final Completion (Closeout Approval Requested)	george2.lacour@pgcps.org	03/03/20	04/30/20	100%
2	Greenbelt ES	FY/20	County Funded	\$148,662	Security Upgrades	Provide and install the following: 1. (58) Fifty-eight IP Network Cameras (24- Outside, 35- Inside) 2. 110TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing	Final Completion (Closeout Approval Requested)	george2.lacour@pgcps.org	03/03/20	04/30/20	100%
2	Greenbelt ES	FY/22	State-HSFF Funded	\$3,360,665	Systemic Upgrades: Misc	Roof Replacement (HSFF)	Final Completion (Closeout Approval Requested)	ricardo.garcia@pgcps.org	06/24/24	09/04/24	100%
2	Greenbelt ES	FY/22	State-HSFF Funded	\$3,360,665	Systemic Upgrades: Misc	Roof Replacement (HSFF)	Final Completion (Closeout Approval Requested)	ricardo.garcia@pgcps.org	06/24/24	09/04/24	100%
2	Greenbelt MS Bus lot (old)	FY/19	County Funded		Central Garage & Transportation	Construction of Administrative Office and Bus Depot at Greenbelt Transportation Facility; Prepare Concept Design for Laurel and Douglass Transportation Facilities	Design	cfloek@pgcps.org			0%
2	Greenbelt MS Bus lot (old)	FY/19	County Funded		Central Garage & Transportation	Construction of Administrative Office and Bus Depot at Greenbelt Transportation Facility; Prepare Concept Design for Laurel and Douglass Transportation Facilities	Design	cfloek@pgcps.org			0%
9	Gwynn Park HS	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-	Final Completion (Closeout)	sunday.owolabi@pgcps.org	06/20/16	08/10/16	100%
9	Gwynn Park HS	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	06/20/16	08/10/16	100%

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
 May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
9	Gwynn Park HS	FY/25	County Funded	\$48,150	Building Repairs: Minor	Gym Fan Installation	Substantially Complete	diego.gonzalezguzman@pgcps.org	10/17/25	11/14/25	100%
9	Gwynn Park HS	FY/25	County Funded	\$48,150	Building Repairs: Minor	Gym Fan Installation	Substantially Complete	diego.gonzalezguzman@pgcps.org	10/17/25	11/14/25	100%
6	H. Winship Wheatley ECC	FY/23	State & County Funded		Systemic Upgrades: HVAC	HVAC Replacement	Design	capital.programs@pgcps.org			
6	H. Winship Wheatley ECC	FY/23	State & County Funded		Systemic Upgrades: HVAC	HVAC Replacement	Design	capital.programs@pgcps.org			
6	H. Winship Wheatley ECC	FY/26	State-ASP Funded	\$690,875	Playgrounds	Playground Replacement	Contractor Procurement	pg_daniel.marks@pgcps.org	06/30/26	09/29/26	
6	H. Winship Wheatley ECC	FY/26	State-ASP Funded	\$690,875	Playgrounds	Playground Replacement	Contractor Procurement	pg_daniel.marks@pgcps.org	06/30/26	09/29/26	
7	Henry Wise Jr. HS	FY/19	County Funded	\$25,000	Kitchen & Food Services	Remove and Replace (1) New Serving Line	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	11/15/23	02/26/21	100%
7	Henry Wise Jr. HS	FY/19	County Funded	\$25,000	Kitchen & Food Services	Remove and Replace (1) New Serving Line	Final Completion (Closeout)	sunday.owolabi@pgcps.org	11/15/23	02/26/21	100%
5	High Bridge ES	FY/15	County Funded	\$300,000	Parking Lots	Major Repairs Driveways, Parking Lots & Entrance Project	Design	capital.programs@pgcps.org	06/19/18	03/30/19	0%
5	High Bridge ES	FY/15	County Funded	\$300,000	Parking Lots	Major Repairs Driveways, Parking Lots & Entrance Project	Design	capital.programs@pgcps.org	06/19/18	03/30/19	0%
5	High Bridge ES	FY/24	County Funded	\$150,000	Abatement	Asbestos Abatement	Contractor Procurement	alex.baylor@pgcps.org	06/20/24		
5	High Bridge ES	FY/24	County Funded	\$150,000	Abatement	Asbestos Abatement	Contractor Procurement	alex.baylor@pgcps.org	06/20/24		
1	High Point HS	FY/19	County Funded	\$50,000	Kitchen & Food Services	Remove and Replace (2) New Serving Lines	Final Completion (Closeout Approval)	sunday.owolabi@pgcps.org	10/01/20	02/26/21	100%
1	High Point HS	FY/19	County Funded	\$231,584	Building Repairs: Minor	Structural Project	Final Completion (Closeout)	joseph.howell@pgcps.org	11/24/20	01/29/21	100%
1	High Point HS	FY/19	County Funded	\$50,000	Kitchen & Food Services	Remove and Replace (2) New Serving Lines	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	10/01/20	02/26/21	100%

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
 May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
1	High Point HS	FY/19	County Funded	\$231,584	Building Repairs: Minor	Structural Project	Final Completion (Closeout)	joseph.howell@pgcps.org	11/24/20	01/29/21	100%
1	High Point HS	FY/24	County Funded	\$450,000	ADA Upgrades	Elevator Modernization	Final Completion (Closeout Approval Requested)	pg_daniel.marks@pgcps.org	06/17/24	09/12/24	100%
1	High Point HS	FY/24	State-Design Services	\$8,570,000	New Schools & Modernizations	Replacement of the existing 318,376 SF,2081-seat high school with a new 423,000 SF high school on the same site with a capacity of 2600 students.	Planning	hiwot.hailellassie@pgcps.org			
1	High Point HS	FY/24	County Funded	\$450,000	ADA Upgrades	Elevator Modernization	Final Completion (Closeout Approval)	pg_daniel.marks@pgcps.org	06/17/24	09/12/24	100%
1	High Point HS	FY/24	State-Design Services	\$8,570,000	New Schools & Modernizations	Replacement of the existing 318,376 SF,2081-seat high school with a new 423,000 SF high school on the same site with a capacity of 2600 students.	Planning	hiwot.hailellassie@pgcps.org			
6	Highland Park ES	FY/17	State & County Funded	\$1,724,000	Systemic Upgrades: HVAC	Piping, Insulation & Boiler Replacement: includes removing the two 1994 hot water boilers, installing two new energy efficient boilers, system pumps and expansion tank. Included is the installation of a limited sprinkler system in that area.	Substantially Complete	nadine.belizaire@pgcps.org	06/28/19	10/25/19	98%
6	Highland Park ES	FY/17	State & County Funded	\$1,724,000	Systemic Upgrades: HVAC	Piping, Insulation & Boiler Replacement: includes removing the two 1994 hot water boilers, installing	Substantially Complete	nadine.belizaire@pgcps.org	06/28/19	10/25/19	98%
6	Highland Park ES	FY/20	County Funded	\$173,326	Security Upgrades	Provide and install the following: 1. (73) Forty-nine IP Network Cameras (28- Outside, 45- Inside) 2. 110TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server	Final Completion (Closeout Approval Requested)	george2.lacour@pgcps.org	07/27/20	08/31/20	100%
6	Highland Park ES	FY/20	County Funded	\$333,167	Systemic Upgrades: HVAC	Chiller Replacement	Final Completion (Closeout Approval Requested)	pg_sean.mccoy@pgcps.org	02/28/24	08/30/24	100%
6	Highland Park ES	FY/20	County Funded	\$173,326	Security Upgrades	Provide and install the following: 1. (73) Forty-nine IP Network Cameras (28- Outside,	Final Completion (Closeout)	george2.lacour@pgcps.org	07/27/20	08/31/20	100%
6	Highland Park ES	FY/20	County Funded	\$333,167	Systemic Upgrades: HVAC	Chiller Replacement	Final Completion (Closeout)	pg_sean.mccoy@pgcps.org	02/28/24	08/30/24	100%
6	Highland Park ES	FY/25	County Funded	\$43,228	Playgrounds	Playground Refurbishment	Final Completion (Closeout Approval Requested)	pg_daniel.marks@pgcps.org	06/09/25	06/13/25	100%
6	Highland Park ES	FY/25	County Funded	\$43,228	Playgrounds	Playground Refurbishment	Final Completion (Closeout)	pg_daniel.marks@pgcps.org	06/09/25	06/13/25	100%

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
 May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
8	Hillcrest Heights ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements. Financial close-out in progress	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	06/20/16	08/17/16	100%
8	Hillcrest Heights ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements. Financial close-out in progress	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	06/20/16	08/17/16	100%
8	Hillcrest Heights ES	FY/24	County Funded	\$600,000	Systemic Upgrades: HVAC	Two (2) Boiler Replacements	Final Completion (Closeout)	pg_sean.mccoey@pgcps.org	06/24/24	10/14/24	100%
8	Hillcrest Heights ES	FY/24	County Funded	\$600,000	Systemic Upgrades: HVAC	Two (2) Boiler Replacements	Final Completion (Closeout Approval)	pg_sean.mccoey@pgcps.org	06/24/24	10/14/24	100%
8	Hillcrest Heights ES	FY/25	State-HSFF Funded	\$2,727,000	Systemic Upgrades: Misc	Roof Replacement (HSFF)	Final Completion (Closeout Approval Requested)	ricardo.garcia@pgcps.org	03/28/25	11/12/25	100%
8	Hillcrest Heights ES	FY/25	State-HSFF Funded	\$2,727,000	Systemic Upgrades: Misc	Roof Replacement (HSFF)	Final Completion (Closeout Approval Requested)	ricardo.garcia@pgcps.org	03/28/25	11/12/25	100%
2	Hollywood ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	06/20/16	08/10/16	100%
2	Hollywood ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-	Final Completion (Closeout)	sunday.owolabi@pgcps.org	06/20/16	08/10/16	100%
2	Hollywood ES	FY/17	State & County Funded	\$766,000	Systemic Upgrades: HVAC	Boiler Replacement	Final Completion (Closeout Approval)	joseph.howell@pgcps.org	06/20/20	08/24/20	100%
2	Hollywood ES	FY/17	State & County Funded	\$766,000	Systemic Upgrades: HVAC	Boiler Replacement	Final Completion (Closeout Approval)	joseph.howell@pgcps.org	06/20/20	08/24/20	100%
2	Hollywood ES	FY/24	Operating Funds	\$150,000	Abatement	Asbestos Abatement	Contractor Procurement	alex.baylor@pgcps.org	06/20/24		
2	Hollywood ES	FY/24	Operating Funds	\$150,000	Abatement	Asbestos Abatement	Contractor Procurement	alex.baylor@pgcps.org	06/20/24		
1	Howard B. Owens Science Center	FY/23	County Funded	\$2,000,000	Building Repairs: Minor	Minor Renovation - Interior and Exterior	Final Completion (Closeout Approval)	pg_daniel.marks@pgcps.org	04/24/23	08/16/24	100%

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
 May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
1	Howard B. Owens Science Center	FY/23	County Funded	\$2,000,000	Building Repairs: Minor	Minor Renovation - Interior and Exterior	Final Completion (Closeout Approval Requested)	pg_daniel.marks@pgcps.org	04/24/23	08/16/24	100%
1	Howard B. Owens Science Center	FY/24	County Funded	\$190,800	Other	Marquee Sign Replacement	Final Completion (Closeout Approval Requested)	pg_daniel.marks@pgcps.org	06/17/24	07/12/24	100%
1	Howard B. Owens Science Center	FY/24	County Funded	\$190,800	Other	Marquee Sign Replacement	Final Completion (Closeout)	pg_daniel.marks@pgcps.org	06/17/24	07/12/24	100%
3	Hyattsville ES	FY/15	County Funded	\$62,477	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project used to be in compliance.	Substantially Complete	sunday.owolabi@pgcps.org	07/24/19	08/14/19	99%
3	Hyattsville ES	FY/15	County Funded	\$62,477	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project used to be in compliance.	Substantially Complete	sunday.owolabi@pgcps.org	07/24/19	08/14/19	99%
3	Hyattsville ES	FY/16	State & County Funded	\$3,472,000	Systemic Upgrades: HVAC	Fan Coil Units & AHUs Replacement	Substantially Complete	capital.programs@pgcps.org	06/19/18	08/31/18	95%
3	Hyattsville ES	FY/16	State & County Funded	\$3,472,000	Systemic Upgrades: HVAC	Fan Coil Units & AHUs Replacement	Substantially Complete	capital.programs@pgcps.org	06/19/18	08/31/18	95%
3	Hyattsville ES	FY/21	County Funded	\$525,000	Kitchen & Food Services	Kitchen Renovation	In Construction	pg_rexie.fernando@pgcps.org			
3	Hyattsville ES	FY/21	County Funded	\$525,000	Kitchen & Food Services	Kitchen Renovation	In Construction	pg_rexie.fernando@pgcps.org			
8	Indian Queen ES	FY/15	State & County Funded	\$4,389,000	Renovations: Pod Conversions	Phase I - Open Space Pod Conversion Renovations / 4 Pods	Substantially Complete	cfloeck@pgcps.org	12/20/16	04/25/18	98%
8	Indian Queen ES	FY/15	State & County Funded	\$4,389,000	Renovations: Pod Conversions	Phase I - Open Space Pod Conversion Renovations / 4 Pods	Substantially Complete	cfloeck@pgcps.org	12/20/16	04/25/18	98%

**Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
May 2026**

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
1	James E. Duckworth SC	FY/15	County Funded	\$300,000	Parking Lots	Major Repairs Driveways, Parking Lots & Entrance Project	Design	capital.programs@pgcps.org	06/19/18	09/30/19	0%
1	James E. Duckworth SC	FY/15	County Funded	\$300,000	Parking Lots	Major Repairs Driveways, Parking Lots & Entrance Project	Design	capital.programs@pgcps.org	06/19/18	09/30/19	0%
1	James H. Harrison ES	FY/20	County Funded	\$148,662	Security Upgrades	Provide and install the following: 1. (57) Fifty-seven IP Network Cameras (23- Outside, 34- Inside) 2.	Final Completion (Closeout	george2.lacour@pgcps.org	12/12/19	01/31/20	100%
1	James H. Harrison ES	FY/20	County Funded	\$148,662	Security Upgrades	Provide and install the following: 1. (57) Fifty-seven IP Network Cameras (23- Outside, 34- Inside) 2. 110TB (useable) TB Storage Server RAID 5 3. UPS for	Final Completion (Closeout Approval	george2.lacour@pgcps.org	12/12/19	01/31/20	100%
1	James H. Harrison ES	FY/26	County Funded	\$250,000	Parking Lots	Parking Lot Refurbishment	Contractor Procurement	pg_sean.mccoey@pgcps.org	06/22/27	08/14/27	
1	James H. Harrison ES	FY/26	County Funded	\$250,000	Parking Lots	Parking Lot Refurbishment	Contractor Procurement	pg_sean.mccoey@pgcps.org	06/22/27	08/14/27	
9	James Madison MS	FY/20	State & County Funded	\$10,421,000	Systemic Upgrades: HVAC	Replacement of HVAC piping system, chiller, cooling tower, four (4) air handling units, 96 mixing boxes, twenty (20) finned tube radiators, fifteen (15) convectors, and controls.	Substantially Complete	anoop.gupta@pgcps.org	06/24/22		98%
9	James Madison MS	FY/20	State & County Funded	\$10,421,000	Systemic Upgrades: HVAC	Replacement of HVAC piping system, chiller, cooling tower, four (4) air handling units, 96 mixing boxes,	Substantially Complete	anoop.gupta@pgcps.org	06/24/22		98%
9	James Madison MS	FY/25	Grant Funded-ESSER	\$3,229,269	Renovations: Misc	Modular Addition	Contractor Procurement	joseph.howell@pgcps.org	08/01/23	07/31/24	99%
9	James Madison MS	FY/25	State-HSFF Funded	\$3,450,680	Systemic Upgrades: Misc	Roof Replacement (HSFF)	Final Completion (Closeout	ricardo.garcia@pgcps.org	04/16/25	10/24/25	100%
9	James Madison MS	FY/25	Grant Funded-ESSER	\$3,229,269	Renovations: Misc	Modular Addition	Contractor Procurement	joseph.howell@pgcps.org	08/01/23	07/31/24	99%
9	James Madison MS	FY/25	State-HSFF Funded	\$3,450,680	Systemic Upgrades: Misc	Roof Replacement (HSFF)	Final Completion (Closeout Approval Requested)	ricardo.garcia@pgcps.org	04/16/25	10/24/25	100%
4	James McHenry ES	FY/25	Operating Funds		Kitchen & Food Services	Construction and installation exterior of walk-in freezer with interior kitchen entry	In Construction	clay.berry@pgcps.org	06/19/25	08/15/25	0%
4	James McHenry ES	FY/25	Operating Funds		Kitchen & Food Services	Construction and installation exterior of walk-in freezer with interior kitchen entry	In Construction	clay.berry@pgcps.org	06/19/25	08/15/25	0%

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
 May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
4	James McHenry ES	FY/26	State-HSFF Funded	\$3,009,200	Systemic Upgrades: Misc	Replacement of approximately 48,000 sf of roof installed in 1999. This is a full roof replacement.	Contractor Procurement	diego.gonzalezguzman@pgcps.org		10/30/26	
4	James McHenry ES	FY/26	County Funded	\$209,000	Code Corrections	Fire Alarm System Replacement	Design	pg_daniel.marks@pgcps.org	06/22/26	03/26/27	
4	James McHenry ES	FY/26	State-HSFF Funded	\$3,009,200	Systemic Upgrades: Misc	Replacement of approximately 48,000 sf of roof installed in 1999. This is a full roof replacement.	Contractor Procurement	diego.gonzalezguzman@pgcps.org		10/30/26	
4	James McHenry ES	FY/26	County Funded	\$209,000	Code Corrections	Fire Alarm System Replacement	Design	pg_daniel.marks@pgcps.org	06/22/26	03/26/27	
8	James Ryder Randall ES	FY/23	County Funded	\$244,500	Code Corrections	Fire Alarm Replacement	Final Completion (Closeout Approval)	pg_daniel.marks@pgcps.org	06/17/24	11/01/24	100%
8	James Ryder Randall ES	FY/23	County Funded	\$244,500	Code Corrections	Fire Alarm Replacement	Final Completion (Closeout Approval)	pg_daniel.marks@pgcps.org	06/17/24	11/01/24	100%
8	James Ryder Randall ES	FY/24	Operating Funds	\$200,000	Abatement	Asbestos Abatement	Contractor Procurement	alex.baylor@pgcps.org	06/20/24		
8	James Ryder Randall ES	FY/24	Operating Funds	\$200,000	Abatement	Asbestos Abatement	Contractor Procurement	alex.baylor@pgcps.org	06/20/24		
8	John Hanson Montessori	FY/23	County Funded	\$315,888	Building Repairs: Major/Emergency	Corridor and Locker Room Replacement	Final Completion (Closeout)	pg_keelan.hendricks@pgcps.org	06/30/22	11/30/22	100%
8	John Hanson Montessori	FY/23	County Funded	\$315,888	Building Repairs: Major/Emergency	Corridor and Locker Room Replacement	Final Completion (Closeout Approval Requested)	pg_keelan.hendricks@pgcps.org	06/30/22	11/30/22	100%
4	Judge Sylvania Woods ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	06/20/16	02/10/17	100%
4	Judge Sylvania Woods ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-	Final Completion (Closeout)	sunday.owolabi@pgcps.org	06/20/16	02/10/17	100%
4	Judge Sylvania Woods ES	FY/18	State & County Funded	\$639,000	Systemic Upgrades: HVAC	Chiller Replacement	Substantially Complete	capital.programs@pgcps.org	06/22/20	08/21/20	95%
4	Judge Sylvania Woods ES	FY/18	State & County Funded	\$639,000	Systemic Upgrades: HVAC	Chiller Replacement	Substantially Complete	capital.programs@pgcps.org	06/22/20	08/21/20	95%
4	Judge Sylvania Woods ES	FY/21	County Funded	\$137,075	Security Upgrades	Install, program and test Sixty-five IP Network Cameras (25- Outside, 40- Inside) with workstation	Final Completion (Closeout)	george2.lacour@pgcps.org	05/03/21	06/30/21	100%

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
 May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
4	Judge Sylvania Woods ES	FY/21	County Funded	\$137,075	Security Upgrades	Install, program and test Sixty-five IP Network Cameras (25- Outside, 40- Inside) with workstation and 43-inch Wall Mounted Live Viewing-Monitor	Final Completion (Closeout Approval Requested)	george2.lacour@pgcps.org	05/03/21	06/30/21	100%
4	Kenmoor ECC	FY/24	County Funded	\$377,969	Exterior Door/Window Upgrades	Exterior Doors and Storefront Windows Replacement	Final Completion (Closeout Approval Requested)	pg_daniel.marks@pgcps.org	07/22/24	02/21/25	100%
4	Kenmoor ECC	FY/24	County Funded	\$377,969	Exterior Door/Window Upgrades	Exterior Doors and Storefront Windows Replacement	Final Completion (Closeout Approval Requested)	pg_daniel.marks@pgcps.org	07/22/24	02/21/25	100%
4	Kenmoor ECC	FY/26	State-ASP Funded	\$397,499	Playgrounds	Playground Replacement	Contractor Procurement	pg_daniel.marks@pgcps.org	06/30/26	09/29/26	
4	Kenmoor ECC	FY/26	State-ASP Funded	\$397,499	Playgrounds	Playground Replacement	Contractor Procurement	pg_daniel.marks@pgcps.org	06/30/26	09/29/26	
4	Kenmoor MS	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-	Final Completion (Closeout)	sunday.owolabi@pgcps.org	09/05/16	01/30/17	100%
4	Kenmoor MS	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-	Final Completion (Closeout)	sunday.owolabi@pgcps.org	09/05/16	01/30/17	100%
4	Kenmoor MS	FY/19	County Funded	\$199,681	Security Upgrades	Provide and install the following: 1. (90) Ninety IP Network Cameras (23- Outside, 67-	Final Completion (Closeout)	george2.lacour@pgcps.org	04/29/19	07/26/19	100%
4	Kenmoor MS	FY/19	County Funded	\$199,681	Security Upgrades	Provide and install the following: 1. (90) Ninety IP Network Cameras (23- Outside, 67- Inside) 2. 130TB Storage Server RAID 5 3. UPS for Storage Server	Final Completion (Closeout Approval Requested)	george2.lacour@pgcps.org	04/29/19	07/26/19	100%
4	Kenmoor MS	FY/24	Operating Funds	\$250,000	Abatement	Asbestos Abatement	Contractor Procurement	alex.baylor@pgcps.org	06/20/24		
4	Kenmoor MS	FY/24	Operating Funds	\$250,000	Abatement	Asbestos Abatement	Contractor Procurement	alex.baylor@pgcps.org	06/20/24		
6	Kettering ES	FY/20	County Funded	\$386,182	Systemic Upgrades: HVAC	Chiller Replacement	In Construction	pg_sean.mccoy@pgcps.org	02/28/24	08/30/24	97%
6	Kettering ES	FY/20	County Funded	\$386,182	Systemic Upgrades: HVAC	Chiller Replacement	In Construction	pg_sean.mccoy@pgcps.org	02/28/24	08/30/24	97%
6	Kettering MS	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-	Final Completion (Closeout)	sunday.owolabi@pgcps.org	06/20/16	01/31/17	100%
6	Kettering MS	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	sunday.owolabi@pgcps.org	06/20/16	01/31/17	100%
6	Kettering MS	FY/19	County Funded	\$276,430	Building Repairs: Major/Emergency	Modular Roof Replacement	Substantially Complete	Lance.Schiemer@pgcps.org	06/30/21	08/30/21	100%

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
 May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
6	Kettering MS	FY/19	County Funded	\$276,430	Building Repairs: Major/Emergency	Modular Roof Replacement	Substantially Complete	Lance.Schiemer@pgcps.org	06/30/21	08/30/21	100%
6	Kettering MS	FY/22	County Funded	\$2,604,262	Renovations: Misc	Provide (10) classroom modular additions	Final Completion (Closeout Approval Requested)	joseph.howell@pgcps.org	08/01/22	08/07/23	100%
6	Kettering MS	FY/22	County Funded	\$2,604,262	Renovations: Misc	Provide (10) classroom modular additions	Final Completion (Closeout Approval Requested)	joseph.howell@pgcps.org	08/01/22	08/07/23	100%
6	Kettering MS	FY/23	Grant Funded (see	\$2,000,000	Systemic Upgrades: HVAC	HVAC Upgrades	Final Completion (Closeout	pg_sean.mccoy@pgcps.org	07/03/24	09/30/24	100%
6	Kettering MS	FY/23	Grant Funded (see	\$2,000,000	Systemic Upgrades: HVAC	HVAC Upgrades	Final Completion (Closeout	pg_sean.mccoy@pgcps.org	07/03/24	09/30/24	100%
5	Kingsford ES	FY/15	County Funded	\$300,000	Parking Lots	Major Repairs Driveways, Parking Lots & Entrance Project	Design	capital.programs@pgcps.org	06/19/18	03/30/19	0%
5	Kingsford ES	FY/15	County Funded	\$300,000	Parking Lots	Major Repairs Driveways, Parking Lots & Entrance Project	Design	capital.programs@pgcps.org	06/19/18	03/30/19	0%
5	Kingsford ES	FY/18	State & County Funded	\$639,000	Systemic Upgrades: HVAC	Chiller Replacement	Substantially Complete	capital.programs@pgcps.org	06/22/20	08/21/20	95%
5	Kingsford ES	FY/18	State & County Funded	\$639,000	Systemic Upgrades: HVAC	Chiller Replacement	Substantially Complete	capital.programs@pgcps.org	06/22/20	08/21/20	95%
6	Lake Arbor ES	FY/19	County Funded	\$137,681	Security Upgrades	Provide and install the following: 1. (60) Sixty IP Network Cameras (17- Outside, 43-	Final Completion (Closeout	george2.lacour@pgcps.org	04/01/19	06/01/19	100%
6	Lake Arbor ES	FY/19	County Funded	\$137,681	Security Upgrades	Provide and install the following: 1. (60) Sixty IP Network Cameras (17- Outside, 43-	Final Completion (Closeout	george2.lacour@pgcps.org	04/01/19	06/01/19	100%
2	Lamont ES	FY/19	County Funded	\$9,283,427	Systemic Upgrades: HVAC	HVAC / Replace the 1964/1966 HVAC system, domestic water piping, plumbing fixtures, 31	Design	pg_rexie.fernando@pgcps.org	06/27/25	06/12/26	0%
2	Lamont ES	FY/19	County Funded	\$500,000	Kitchen & Food Services	Kitchen Renovation: Remove existing kitchen equipment and replace/upgrade with new.	Final Completion (Closeout Approval	ricardo.garcia@pgcps.org	06/27/22	08/26/22	100%
2	Lamont ES	FY/19	County Funded	\$9,283,427	Systemic Upgrades: HVAC	HVAC / Replace the 1964/1966 HVAC system, domestic water piping, plumbing fixtures, 31 windows, 29 exterior doors, ceilings, lighting, and fire alarm system, and install a sprinkler system.	Design	pg_rexie.fernando@pgcps.org	06/27/25	06/12/26	0%
2	Lamont ES	FY/19	County Funded	\$500,000	Kitchen & Food Services	Kitchen Renovation: Remove existing kitchen equipment and replace/upgrade with new.	Final Completion (Closeout	ricardo.garcia@pgcps.org	06/27/22	08/26/22	100%

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
 May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
2	Lamont ES				Systemic Upgrades: HVAC	HVAC Replacement and Building Envelope Renovation	Scope Development	pg_rexie.fernando@pgcps.org			
2	Lamont ES				Systemic Upgrades: HVAC	HVAC Replacement and Building Envelope Renovation	Scope Development	pg_rexie.fernando@pgcps.org			
6	Largo HS	FY/14	State & County Funded	\$981,125	Systemic Upgrades: HVAC	Air Conditioning Initiative (ACI) - Provide air conditioning in the 1970 school building gymnasium	Substantially Complete	kmuse@pgcps.org	06/14/17	10/13/17	98%
6	Largo HS	FY/14	State & County Funded	\$981,125	Systemic Upgrades: HVAC	Air Conditioning Initiative (ACI) - Provide air conditioning in the 1970 school building gymnasium	Substantially Complete	kmuse@pgcps.org	06/14/17	10/13/17	98%
6	Largo HS	FY/15	State & County Funded	\$964,000	Renovations: Career Academy	Secondary School Reform (SSR) - Renovations for the academy of Business and Finance	Substantially Complete	hiwot.haileselassie@pgcps.org	12/28/16	10/01/19	99%
6	Largo HS	FY/15	State & County Funded	\$4,261,000	Renovations: Pod Conversions	Open Space Pod Conversion Renovations / 5 Pods-Phase I	Substantially Complete	hiwot.haileselassie@pgcps.org	12/28/16	08/12/18	99%
6	Largo HS	FY/15	State & County Funded	\$964,000	Renovations: Career Academy	Secondary School Reform (SSR) - Renovations for the academy of Business and Finance	Substantially Complete	hiwot.haileselassie@pgcps.org	12/28/16	10/01/19	99%
6	Largo HS	FY/15	State & County Funded	\$4,261,000	Renovations: Pod Conversions	Open Space Pod Conversion Renovations / 5 Pods-Phase I	Substantially Complete	hiwot.haileselassie@pgcps.org	12/28/16	08/12/18	99%
6	Largo HS	FY/16	State & County Funded	\$3,586,000	Renovations: Career Academy	Secondary School Reform (SSR) - Renovations for the academy of Health & Biosciences.	Substantially Complete	hiwot.haileselassie@pgcps.org	06/15/17	08/19/20	99%
6	Largo HS	FY/16	State & County Funded	\$3,586,000	Renovations: Career Academy	Secondary School Reform (SSR) - Renovations for the academy of Health & Biosciences.	Substantially Complete	hiwot.haileselassie@pgcps.org	06/15/17	08/19/20	99%
1	Laurel Bus Lot	FY/15	County Funded	\$285,700	Central Garage & Transportation	Laurel Bus Lot Project - A revised Capital Plan needs to be developed with the Department of Transportation and Central Garage.	Planning	cfloek@pgcps.org			0%

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
 May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
1	Laurel Bus Lot	FY/15	County Funded	\$285,700	Central Garage & Transportation	Laurel Bus Lot Project - A revised Capital Plan needs to be developed with the Department of Transportation and Central Garage.	Planning	cfloeck@pgcps.org			0%
1	Laurel HS	FY/20	Grant Funded (see description)	\$6,500,000	Athletic Improvements	Football Stadium Renovation	Final Completion (Closeout Approval Requested)	william5.smith@pgcps.org		02/16/24	
1	Laurel HS	FY/20	Grant Funded (see	\$6,500,000	Athletic Improvements	Football Stadium Renovation	Final Completion (Closeout	william5.smith@pgcps.org		02/16/24	
3	Lewisdale ES	FY/16	State & County Funded	\$289,000	Systemic Upgrades: HVAC	RTU Replacement - The scope of this project will be to remove and replace 7 Roof Top Units (RTUs) in the 1953 building. The new units will have digital control and tie-in to our EMS.	Substantially Complete	joseph.howell@pgcps.org	06/01/19	08/30/19	100%
3	Lewisdale ES	FY/16	State & County Funded	\$289,000	Systemic Upgrades: HVAC	RTU Replacement - The scope of this project will be to remove and replace 7 Roof Top Units (RTUs) in the 1953 building. The new units will have digital control and tie-in to our EMS.	Substantially Complete	joseph.howell@pgcps.org	06/01/19	08/30/19	100%
7	Longfields ES	FY/22	County Funded	\$500,000	Renovations: Misc	Staged Renovation	Planning	sunday.owolabi@pgcps.org	06/14/24		0%
7	Longfields ES	FY/22	County Funded	\$500,000	Renovations: Misc	Staged Renovation	Planning	sunday.owolabi@pgcps.org	06/14/24		0%
2	Magnolia ES	FY/23	County Funded	\$205,000	Parking Lots	Parking Lot & Existing Areas	Final Completion (Closeout Approval Requested)	pg_daniel.marks@pgcps.org	06/19/23	08/11/23	100%
2	Magnolia ES	FY/23	County Funded	\$205,000	Parking Lots	Parking Lot & Existing Areas	Final Completion (Closeout	pg_daniel.marks@pgcps.org	06/19/23	08/11/23	100%
2	Magnolia ES	FY/24	County Funded	\$210,000	Code Corrections	Fire Alarm System Replacement	Final Completion (Closeout	pg_daniel.marks@pgcps.org	06/30/25	11/05/25	100%
2	Magnolia ES	FY/24	County Funded	\$210,000	Code Corrections	Fire Alarm System Replacement	Final Completion (Closeout	pg_daniel.marks@pgcps.org	06/30/25	11/05/25	100%
2	Margaret Brent SC	FY/21	County Funded	\$2,000,000	New Schools & Modernizations	Renovation/Replacement	Planning	william5.smith@pgcps.org			
2	Margaret Brent SC	FY/21	County Funded	\$2,000,000	New Schools & Modernizations	Renovation/Replacement	Planning	william5.smith@pgcps.org			

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
 May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
9	Marlton ES	FY/17	State & County Funded	\$875,000	Systemic Upgrades: HVAC	Piping Insulation Replacement & Controls Upgrade: includes total replacement of the existing pneumatic controls. Also includes the replacement of valves,	Substantially Complete	pg_rexie.fernando@pgcps.org	06/25/18	08/24/18	98%
9	Marlton ES	FY/17	State & County Funded	\$875,000	Systemic Upgrades: HVAC	Piping Insulation Replacement & Controls Upgrade: includes total replacement of the existing pneumatic controls. Also includes the replacement of valves, dampers, sensors, actuators, and safety controls.	Substantially Complete	pg_rexie.fernando@pgcps.org	06/25/18	08/24/18	98%
1	Martin Luther King Jr. MS	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-	Final Completion (Closeout	sunday.owolabi@pgcps.org	06/20/16	08/15/16	100%
1	Martin Luther King Jr. MS	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-	Final Completion (Closeout	sunday.owolabi@pgcps.org	06/20/16	08/15/16	100%
1	Martin Luther King Jr. MS	FY/23	County Funded	\$70,000	Building Repairs: Minor	Dance Floor Replacement	Final Completion (Closeout Approval Requested)	pg_keelan.hendricks@pgcps.org	07/20/23	08/18/23	100%
1	Martin Luther King Jr. MS	FY/23	County Funded	\$70,000	Building Repairs: Minor	Dance Floor Replacement	Final Completion (Closeout	pg_keelan.hendricks@pgcps.org	07/20/23	08/18/23	100%
1	Martin Luther King Jr. MS	FY/26	State & County Funded	\$3,428,811	Systemic Upgrades: Misc	Replace the 1972 89,899 sf built-up roof.	Planning	ricardo.garcia@pgcps.org			
1	Martin Luther King Jr. MS	FY/26	State & County Funded	\$3,428,811	Systemic Upgrades: Misc	Replace the 1972 89,899 sf built-up roof.	Planning	ricardo.garcia@pgcps.org			
3	Mary Harris Jones ES	FY/19	County Funded	\$140,895	Security Upgrades	Provide and install the following: 1. (61) Sixty One IP Network Cameras (17- Outside, 44- Inside) 2. 110TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-	Final Completion (Closeout Approval Requested)	george2.lacour@pgcps.org	08/08/19	04/01/20	100%
3	Mary Harris Jones ES	FY/19	County Funded	\$140,895	Security Upgrades	Provide and install the following: 1. (61) Sixty One IP Network Cameras (17- Outside, 44- Inside) 2. 110TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing-Monitor PC	Final Completion (Closeout Approval Requested)	george2.lacour@pgcps.org	08/08/19	04/01/20	100%
6	Maya Angelou French Immersion	FY/22	County Funded	\$132,416	ADA Upgrades	Lift Replacement	Final Completion (Closeout Approval Requested)	pg_daniel.marks@pgcps.org	09/16/24	10/18/24	100%
6	Maya Angelou French Immersion	FY/22	County Funded	\$132,416	ADA Upgrades	Lift Replacement	Final Completion (Closeout Approval Requested)	pg_daniel.marks@pgcps.org	09/16/24	10/18/24	100%
6	Maya Angelou French Immersion	FY/26	County Funded	\$200,000	Parking Lots	Parking Lot Refurbishment	Contractor Procurement	pg_sean.mccoy@pgcps.org	06/22/27	08/14/27	

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
 May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
6	Maya Angelou French Immersion	FY/26	County Funded	\$200,000	Parking Lots	Parking Lot Refurbishment	Contractor Procurement	pg_sean.mccoey@pgcps.org	06/22/27	08/14/27	
5	Meadowbrook ES	FY/24	County Funded	\$116,510	ADA Upgrades	Lift Installation - Structural Alterations in Stairwell	In Construction	pg_daniel.marks@pgcps.org	06/22/26	08/14/26	90%
5	Meadowbrook ES	FY/24	County Funded	\$116,510	ADA Upgrades	Lift Installation - Structural Alterations in Stairwell	In Construction	pg_daniel.marks@pgcps.org	06/22/26	08/14/26	90%
9	Melwood ES	FY/15	State & County Funded	\$1,661,000	Renovations: Pod Conversions	Open Space Pod Conversion Renovations / 2 Pods	Substantially Complete	pg_rexie.fernando@pgcps.org	06/15/17	08/18/17	95%
9	Melwood ES	FY/15	State & County Funded	\$1,661,000	Renovations: Pod Conversions	Open Space Pod Conversion Renovations / 2 Pods	Substantially Complete	pg_rexie.fernando@pgcps.org	06/15/17	08/18/17	95%
9	Melwood ES	FY/17	State & County Funded	\$575,000	Exterior Door/Window Upgrades	Storefront & Window Wall Replacement: A total of 19 windows and 1 double door will be replaced. Includes demolishing existing storefront system and remove all related debris, install new aluminum storefront system and entrance doors.	Final Completion (Closeout Approval Requested)	ricardo.garcia@pgcps.org	08/20/18	02/22/19	100%
9	Melwood ES	FY/17	State & County Funded	\$575,000	Exterior Door/Window Upgrades	Storefront & Window Wall Replacement: A total of 19 windows and 1 double door will be replaced. Includes demolishing existing storefront system and remove all related debris, install new aluminum storefront system and entrance doors.	Final Completion (Closeout Approval Requested)	ricardo.garcia@pgcps.org	08/20/18	02/22/19	100%
9	Melwood ES	FY/19	County Funded	\$1,700,000	Parking Lots	Parking Lot Improvements	Design	anoop.gupta@pgcps.org	02/02/24	08/14/26	0%
9	Melwood ES	FY/19	County Funded	\$1,700,000	Parking Lots	Parking Lot Improvements	Design	anoop.gupta@pgcps.org	02/02/24	08/14/26	0%
9	Melwood ES	FY/20	County Funded	\$109,738	Security Upgrades	Provide and install the following: 1. (42) Forty-nine IP Network Cameras (17- Outside, 25- Inside) 2. 90TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server	Final Completion (Closeout Approval Requested)	george2.lacour@pgcps.org	12/02/19	02/28/20	100%
9	Melwood ES	FY/20	County Funded	\$109,738	Security Upgrades	Provide and install the following: 1. (42) Forty-nine IP Network Cameras (17- Outside, 25- Inside) 2. 90TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server	Final Completion (Closeout Approval Requested)	george2.lacour@pgcps.org	12/02/19	02/28/20	100%

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
 May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
9	Melwood ES	FY/26	State & County Funded	\$3,550,000	Systemic Upgrades: Misc	Replace the 1996 65,985 sf built-up roof.	Planning	ricardo.garcia@pgcps.org			
9	Melwood ES	FY/26	County Funded	\$200,200	Code Corrections	Fire Alarm System Replacement	Design	pg_daniel.marks@pgcps.org	09/21/26	12/18/26	
9	Melwood ES	FY/26	State & County Funded	\$3,550,000	Systemic Upgrades: Misc	Replace the 1996 65,985 sf built-up roof.	Planning	ricardo.garcia@pgcps.org			
9	Melwood ES	FY/26	County Funded	\$200,200	Code Corrections	Fire Alarm System Replacement	Design	pg_daniel.marks@pgcps.org	09/21/26	12/18/26	
9	Melwood ES				Parking Lots	Parking Lot and Bus Loop Improvements	Scope Development	anoop.gupta@pgcps.org			
9	Melwood ES				Parking Lots	Parking Lot and Bus Loop Improvements	Scope Development	anoop.gupta@pgcps.org			
5	Mullikin Bus Lot	FY/19	County Funded	\$250,000	Central Garage & Transportation	Construction of Administrative Office and Bus Depot at Mullikin Transportation Facility; Prepare Concept Design for Laurel and Douglass Transportation Facilities	In Construction	don.howerton@pgcps.org	04/01/24	06/01/26	99%
5	Mullikin Bus Lot	FY/19	County Funded	\$250,000	Central Garage & Transportation	Construction of Administrative Office and Bus Depot at Mullikin Transportation Facility; Prepare Concept Design for Laurel and Douglass Transportation Facilities	In Construction	don.howerton@pgcps.org	04/01/24	06/01/26	99%
3	New Northern Adelphi Area HS	FY/26	State-Design Services	\$10,168,000	New Schools & Modernizations	Construction of a new 369,806 SF and 2,600 student high school in the Adelphi area to alleviate current overcrowding in neighboring schools and meet the	Design	hiwot.hailellassie@pgcps.org			0%
3	New Northern Adelphi Area HS	FY/26	State-Design Services	\$10,168,000	New Schools & Modernizations	Construction of a new 369,806 SF and 2,600 student high school in the Adelphi area to alleviate current overcrowding in neighboring schools and meet the demands of projected enrollment.	Design	hiwot.hailellassie@pgcps.org			0%
3	Nicholas Orem MS	FY/14	State & County Funded	\$1,000,000	Systemic Upgrades: HVAC	Condensate Piping Infrastructure Replacement	Substantially Complete	kmuse@pgcps.org	06/14/17	10/30/17	99%
3	Nicholas Orem MS	FY/14	State & County Funded	\$1,000,000	Systemic Upgrades: HVAC	Condensate Piping Infrastructure Replacement	Substantially Complete	kmuse@pgcps.org	06/14/17	10/30/17	99%
3	Nicholas Orem MS	FY/22	County Funded	\$800,000	Kitchen & Food Services	Kitchen Renovation	Final Completion (Closeout Approval Requested)	ricardo.garcia@pgcps.org	06/24/25	10/02/25	100%

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
 May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
3	Nicholas Orem MS	FY/22	County Funded	\$800,000	Kitchen & Food Services	Kitchen Renovation	Final Completion (Closeout)	ricardo.garcia@pgcps.org	06/24/25	10/02/25	100%
3	Nicholas Orem MS	FY/26	County Funded	\$400,000	Building Repairs: Minor	Multipurpose Room Stage Refurbishment	Contractor Procurement	pg_daniel.marks@pgcps.org	06/22/26	08/14/26	
3	Nicholas Orem MS	FY/26	County Funded	\$400,000	Building Repairs: Minor	Multipurpose Room Stage Refurbishment	Contractor Procurement	pg_daniel.marks@pgcps.org	06/22/26	08/14/26	
7	North Forestville ES	FY/14	State & County Funded	\$800,000	Systemic Upgrades: HVAC	Condensate Piping Infrastructure Replacement	Substantially Complete	kmuse@pgcps.org	06/14/17	09/29/17	99%
7	North Forestville ES	FY/14	State & County Funded	\$800,000	Systemic Upgrades: HVAC	Condensate Piping Infrastructure Replacement	Substantially Complete	kmuse@pgcps.org	06/14/17	09/29/17	99%
7	North Forestville ES	FY/17	State & County Funded	\$639,000	Systemic Upgrades: HVAC	Boiler Replacement: includes removal of two 60 hp steam boilers and 1/4 hp return pumps and replacing them with two new energy efficient 60 hp boilers, boiler feed system and return pumps.	Substantially Complete	nadine.belizaire@pgcps.org	10/05/18	12/28/18	99%
7	North Forestville ES	FY/17	State & County Funded	\$639,000	Systemic Upgrades: HVAC	Boiler Replacement: includes removal of two 60 hp steam boilers and 1/4 hp return pumps and replacing them with two new energy efficient 60 hp boilers, boiler feed system and return pumps.	Substantially Complete	nadine.belizaire@pgcps.org	10/05/18	12/28/18	99%
5	Northview ES	FY/21	County Funded	\$200,000	Security Upgrades	New IP Camera system	Scope Development	george2.lacour@pgcps.org			
5	Northview ES	FY/21	County Funded	\$200,000	Security Upgrades	New IP Camera system	Scope Development	george2.lacour@pgcps.org			
3	Northwestern HS	FY/15	County Funded	\$797,000	Renovations: Career Academy	Secondary School Reform (SSR) - Renovations for the academic academies of Business & Finance	Contractor Procurement	hiwot.haileselassie@pgcps.org	06/23/20		0%
3	Northwestern HS	FY/15	County Funded	\$797,000	Renovations: Career Academy	Secondary School Reform (SSR) - Renovations for the academic academies of Business & Finance	Contractor Procurement	hiwot.haileselassie@pgcps.org	06/23/20		0%
3	Northwestern HS	FY/16	County Funded	\$98,000	Renovations: Career Academy	Secondary School Reform (SSR) - This renovation will be for the Academy for Performing Arts.	Contractor Procurement	hiwot.haileselassie@pgcps.org	06/23/20	08/15/20	0%
3	Northwestern HS	FY/16	County Funded	\$98,000	Renovations: Career Academy	Secondary School Reform (SSR) - This renovation will be for the Academy for Performing Arts.	Contractor Procurement	hiwot.haileselassie@pgcps.org	06/23/20	08/15/20	0%
3	Northwestern HS	FY/21	County Funded	\$497,321	Security Upgrades	Install program and test Two hundred Forty-five IP Network Cameras (46- Outside, 195- Inside) with workstation and 43-inch Wall Mounted Live Viewing-Monitor	In Construction	george2.lacour@pgcps.org	03/08/21	06/30/21	

Prince George's County Public Schools
STATUS OF ACTIVE CAPITAL PROJECTS
May 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
3	Northwestern HS	FY/21	County Funded	\$497,321	Security Upgrades	Install program and test Two hundred Forty-five IP Network Cameras (46- Outside, 195- Inside) with workstation and 43-inch Wall Mounted Live Viewing-Monitor	In Construction	george2.lacour@pgcps.org	03/08/21	06/30/21	
3	Northwestern HS	FY/26	County Funded	\$138,830	Building Repairs: Minor	Chiller Repairs	Contractor Procurement	pg_sean.mccoy@pgcps.org			
PROJECT PHASES											
Planning - Project plans are documented, the project deliverables and requirements are defined with stakeholders and reviewing agencies, and the project schedule is created.											
8	Oxon Hill ES	FY/23	Operating Funds	\$1,000,000	Systemic Upgrades: HVAC	Chiller and Cooling Tower Replacement	Substantially Complete	garth.deitzer@pgcps.org	07/03/23		80%
